

JACKSONVILLE DISTRICT PROGRAM OVERVIEW

DoDAAC/Office Code: W912EP

January 2024

Working Today to Build a Better Tomorrow



U.S. ARMY



US Army Corps
of Engineers





U.S. ARMY

BRIEFING PURPOSE/AGENDA



- Area of Responsibility
- Program Overview
- South Florida Ecosystem Restoration - Integrated Delivery Schedule Overview
- Upcoming Contracting Opportunities
- Jacksonville District Small Business Office Information & Resources

<http://www.saj.usace.army.mil/>

JACKSONVILLE DISTRICT

Our Vision

- A team of professionals making tomorrow better.

Our Mission

- Deliver value to the Nation by anticipating needs and collaboratively engineering solutions that support national security, energize our economy, and increase resiliency.

Our Area of Responsibility

- Florida
- Georgia
- Puerto Rico
- U.S. Virgin Islands

AREAS OF RESPONSIBILITY

CIVIL WORKS

- Portions of Florida and Georgia (defined by watersheds)

REGULATORY


- Florida
- Puerto Rico and the Antilles

REAL ESTATE AND MOBILIZATION



- Portions of Florida and Georgia

MILITARY

- Florida
 - Jacksonville covers SRM and IIS only
 - Mobile District covers MILCON
- Puerto Rico, Antilles, and Caribbean Basin
 - Jacksonville responsible for Project Management of MILCON, IIS & SRM.
 - Note: TF VIPR is responsible for construction/contract admin in PR & VI

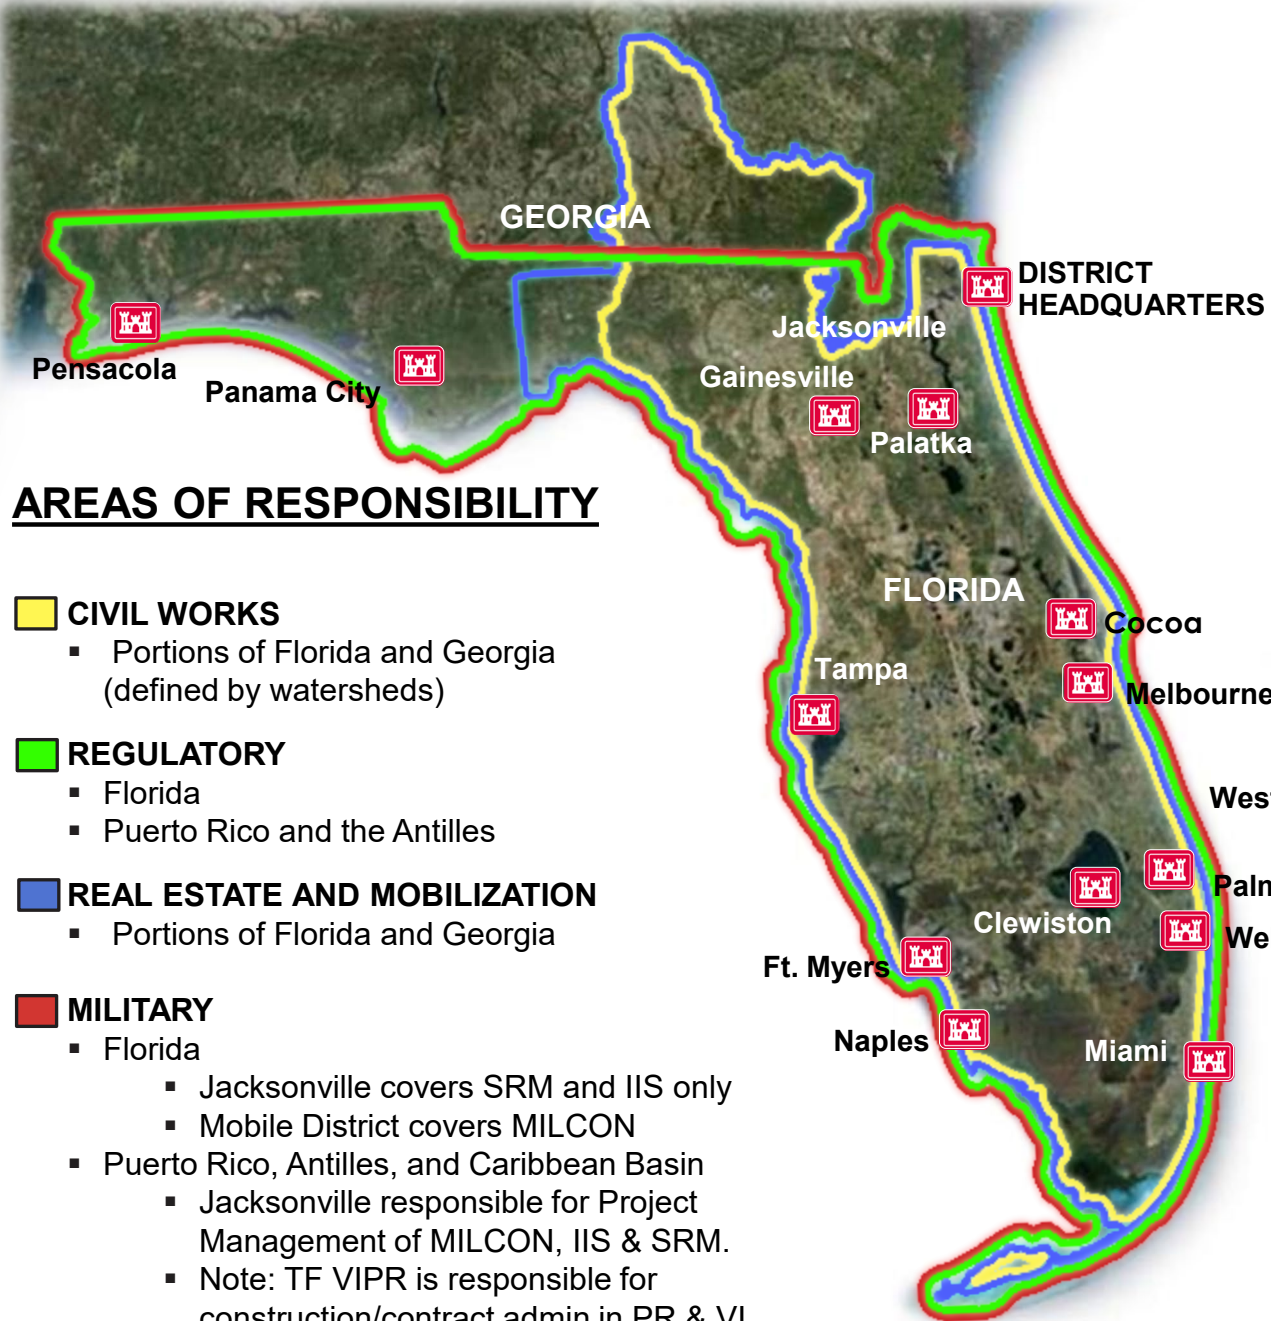

JACKSONVILLE DISTRICT PROGRAMS BY FISCAL YEAR (FY) 2020 - 2024

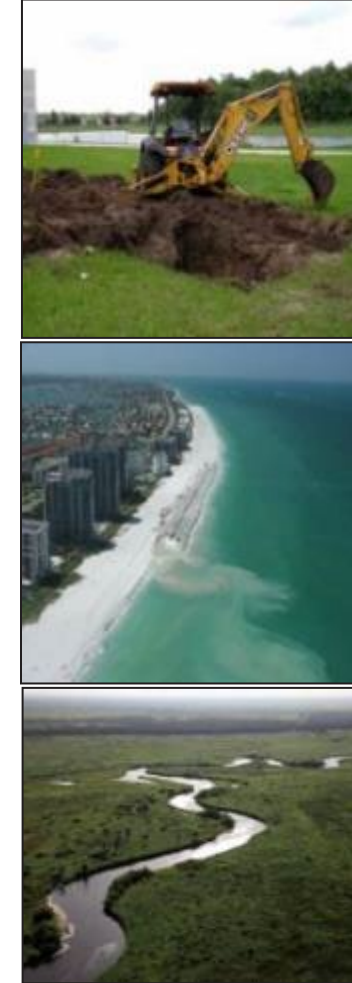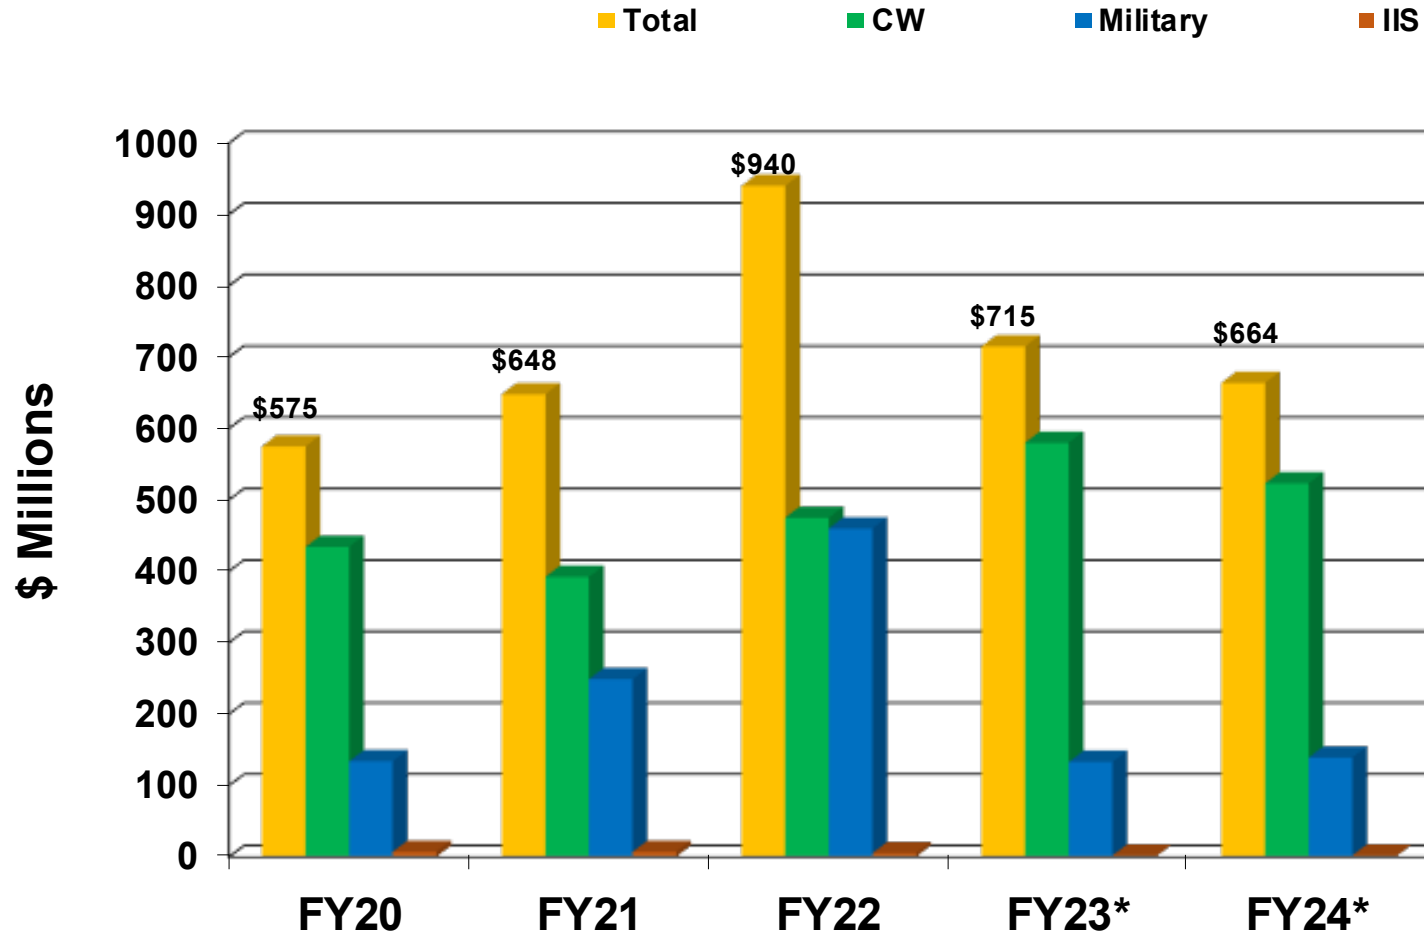

Summary does not include SAJ Regulatory Program, \$ amounts are in millions

* FY23 OMNIBUS

* FY24 PBUD

All other Fiscal Years reflect actual allocations



U.S. ARMY



OUR MISSION AREAS

Deliver value to the Nation by anticipating needs & collaboratively engineering solutions that support national security, energize our economy, & increase resiliency.

- Navigation
- Flood/Coastal Storm Risk Management
- Ecosystem Restoration
- Operations/Recreation
- Contingency Operations
- Real Estate
- Military/Interagency & International Services
- Regulatory





U.S. ARMY

South Florida Ecosystem Restoration (SFER)



INTEGRATED DELIVERY SCHEDULE 2023 UPDATE

SOUTH FLORIDA ECOSYSTEM RESTORATION | CENTRAL AND SOUTHERN FLORIDA COMPREHENSIVE EVERGLADES RESTORATION PLAN



The **Comprehensive Everglades Restoration Plan (CERP)** is the largest aquatic ecosystem restoration effort in the nation, spanning over 18,000 square miles, and is designed to improve the health of more than 2.4 million acres. The Integrated Delivery Schedule (IDS) is a forward-looking snapshot of upcoming planning, design, and construction schedules and programmatic costs at a "top" line level for the South Florida Ecosystem Restoration (SFER) Program – including CERP, Modified Water Deliveries to Everglades National Park, the Critical Projects Program, Kissimmee River Restoration, and non-CERP Central and Southern Florida (C&SF) projects.

The IDS reflects the sequencing strategy for planning, design, and construction and does not include costs for work completed in other fiscal years or land acquisition. The IDS does not require an agency action and is not a decision document. It is a tool that provides information to decision-makers – a living document that is updated as

needed to reflect progress and/or program changes. The IDS synchronizes program and project priorities with the State of Florida and achieves the CERP restoration objectives at the earliest practicable time, consistent with funding constraints and the interdependencies between project components.


Although non-CERP and Foundation projects upon which the CERP is dependent are reflected in the IDS schedule, they are not included in the funding scenario. These projects are funded through other program authorities or by other entities. Restoration projects by others are also not included but are considered during planning.

Note: The IDS serves the purpose of the Master Sequencing and Implementation Plan (MISP) described in the original CERP plan (Yellow Book). Funding shown for Fiscal Year 25 (Fiscal Year, October 1 - September 30) and beyond is only notional, representing approximate funding levels that would be needed to sustain the work displayed in the IDS for any particular fiscal year. The funding does not represent a commitment by the Administration to budget the amounts shown.

Projects completed in prior years have been removed from the 2023 IDS.

SOUTH FLORIDA ECOSYSTEM RESTORATION (SFER) INVESTMENT THROUGH FY2022 (Millions)					
	FEDERAL			NON-FEDERAL MULTIPLE AGENCIES	GRAND TOTAL
	USACE	DOI	TOTAL		
Modified Water Deliveries to ENP	\$ 78	\$ 317	\$ 395	-	\$ 395
Critical Projects	\$ 89	-	\$ 89	\$ 88	\$ 177
Kissimmee River Restoration	\$ 409	-	\$ 409	\$ 401	\$ 810
C&SF Non-CERP	\$ 780	\$ 52	\$ 831	\$ 227	\$ 1,059
C&SF CERP	\$ 2,168	\$ 112	\$ 2,281	\$ 2,579	\$ 4,860
C&SF CERP, to be credited	-	-	-	\$ 894	\$ 894
TOTAL SFER	\$ 3,524	\$ 482	\$ 4,005	\$ 4,190	\$ 8,195
Herbert Hoover Dike Restoration Strategies and ECP	\$ 1,511	-	\$ 1,511	\$ 100	\$ 1,611
	-	-	-	\$ 2,446	\$ 2,446

IDS PROJECT LOCATIONS (NOT TO SCALE)
(Refer to Project Locator in Table)

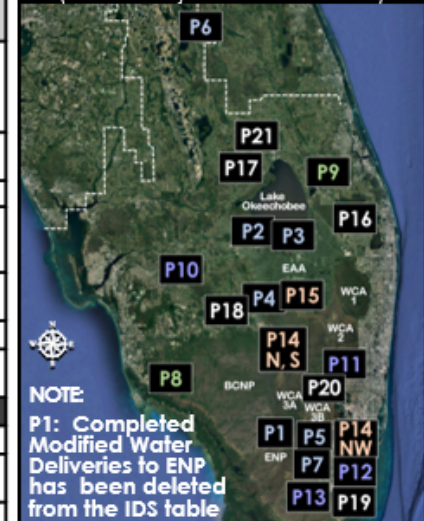

NOTE:

P1: Completed Modified Water Deliveries to ENP has been deleted from the IDS table

Non-federal
Federal
Fiscal Closeout
Monitoring

++	Does not reflect budgetary development dollars or capability
W	Expected WRDA year
•XXXX•	Project Implementation Report
•XXXX•	Project Implementation Report with Exemption

•••••	Design, PPA Execution, Real Estate Acquisition
•••••	Construction (Initiated by award of construction contract)
•••••	Operational Plan
•••••	Operational Testing and Monitoring Period

SCAN THIS CODE FOR QUICK ACCESS TO A DIGITAL COPY OF THE IDS



Design

Award

Construction



IDS 2023: NON-CERP AND FOUNDATION PROJECTS




PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	FISCAL YEAR (dollars in millions) ¹													
			2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W	
			NON-CERP AND FOUNDATION													
P2	Herbert Hoover Dike ³	N/A Non-CERP	—	—●												
P3	Lake Okeechobee System Operating Manual ³		oooo	oooo	oo●											
P4	Restoration Strategies ³		—	—	—	—●										
P5	Tamiami Trail Next Steps (TTNS) Phase 2 ³		—	—	—	—	—●									
P6	KRR-Development of Operational Transition Plan/Evaluation Monitoring		oooo	oooo	oooo	oooo	ooo●△△△	△△△△	△△△△	△△△△	△△△△	△△△△	△△●			
P7	C-111 South Dade Construction (complete)											●□□□●				
	C-111 South Dade - S-332 B Pump Station Replacement		●●●●●	●●●●●	●●●●—	—	—●	●●●●●								
	C-111 South Dade - S-332 C Pump Station Replacement	●●●●●	●●●●●	●●●●●	●●●●●	—	—	—●●●●	●●●							



Design

Award

Construction

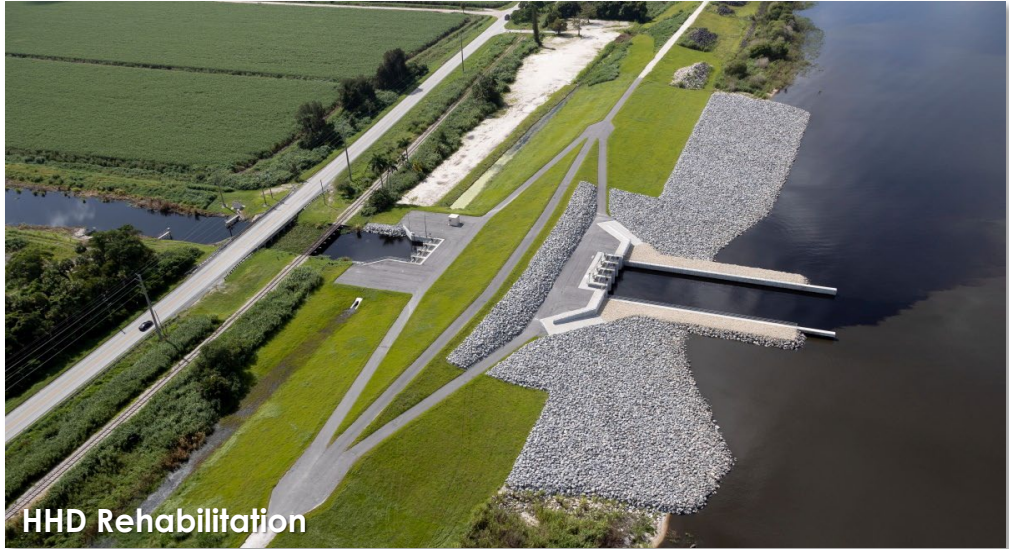

HHD Rehabilitation



Tamiami Trail Bridge



Kissimmee River Restoration



U.S. ARMY

IDS 2023: CERP GENERATION 1, WRDA 2007



PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	FISCAL YEAR (dollars in millions) ¹												
			2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W
CERP GENERATION 1 (AUTHORIZED IN WRDA 2007)															
P8	Picayune Strand Restoration	OPE					●□□□□	□□□□●							
	Flood Protection Features - Conveyance		_____	_____	_____●●	○○○○●									
	Flood Protection Features - Levee		_____	_____	_____●										
	Road Removal		_____	_____●											
	Canal Plugging		●_____	_____	_____	_____●									
P9	Indian River Lagoon-South														
	C-44 Reservoir	B	○○○○○○	○○○○○○	○○○○○○	○○○○○○	○○●								
	C-44 STA and Pump Station	B	○○○○●												
	C-23/24 Reservoir North	UU Phase 1	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	
	C-23/24 Reservoir South	UU Phase 1	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	
	C-23/24 STA	UU Phase 1	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	
	C-25 Reservoir and STA	UU Phase 1	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	
	C-23 Estuary Discharge Diversion		●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	●●●●●●	
Natural Water Quality Storage Areas, Muck Removal and Artificial Habitat Creation (Phase 2) - Director's Report and PPA - After Execution, SFWMD Leading Design and Construction		UU Phase 2	●●●●●●	●●●●●●	●●●●●●										




C-44 Reservoir



C-23/24 STA



Picayune Strand



Picayune Strand
(Conservancy of Southwest Florida)



U.S. ARMY

IDS 2023: CERP GENERATION 2, WRDA 2014



PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	FISCAL YEAR (dollars in millions) ¹												
			2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W
CERP GENERATION 2 (AUTHORIZED IN WRDA 2014)															
P10	Caloosahatchee River (C-43) West Basin Storage	D						●□□□□	□□□□●						
	C-43 Reservoir		—	—	—	—●	◇◇◇◇◇	◇◇◇◇●							
	C-43 Pump Station		—●	◇◇◇◇◇	◇◇◇◇●										
P11	Broward County Water Preserve Areas														
	C-11 Impoundment	Q	●●●●●	●●●●●	●●●●●	—	—	—	—	—	—	—●	◇◇◇◇◇	◇◇◇◇●	
	WCA 3A and 3B Seepage Management	O			●●●●●	●●●●●	●●●●●	●●●●●	—	—	—	—●	◇◇◇◇◇	◇◇◇◇●	
	C-9 Impoundment	R				●●●●●	●●●●●	●●●●●	—	—	—	—	—	—	—●
P12	Biscayne Bay Coastal Wetlands	FFF, OPE Phase 1					●□□□□	□□□□●							
	L-31 East Flow-way S-709 Pump Station (PS)		—	—●◇◇	◇◇◇◇●										
	L-31 East Flow-way S-705 PS		—	—	—●◇◇	◇◇◇◇●									
	L-31 East Flow-way S-703 PS		—	—	—●◇◇	◇◇◇◇●									
	L-31 East Flow-way S-710 PS, S-711 PS, and C-711W Seepage Canal		—	—	—	—●◇◇	◇◇◇◇●								
	Cutler Wetlands		—●—	—	—	—●	◇◇◇◇●								
P13	C-111 Spreader Canal Western Project (Requires PPA – to be Reconciled In Parallel to BBSEER) SFWMD Led Design and Construction	WW Phase 1				●●●●●	●□□□□	□□□□●							
PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W



C-43 Reservoir Pump Intake Station



C-43 Reservoir Construction



Biscayne Bay Coastal Wetlands (Kiewit)



IDS 2023: CENTRAL EVERGLADES PLANNING PROJECT, WRDA 2016



PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	FISCAL YEAR (dollars in millions) ¹												
			2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W
CERP GENERATION 3 (AUTHORIZED IN WRDAS 2016, 2018, 2020)															
P14	Central Everglades Planning Project														
	CEPP South: Additional Outlet Structures Needed to Move More Water South	AA, FF, H, QQ													
	Validation Report - S-152 and Backfill Treatments		*****	***●											
	S-152 and Existing Backfill Treatments (Permanent)		●○○○○○	○○●											
P14S	S-631, S-632, S-633 Structures; Gap in L-67C Levee; L- 67A Spoil Pile Removal		*****	●————	————	————	————	————●○○	○○○○○●						
	S-356E Pump Station and S-334E Gated Spillway		*****	*****	●●●●●	————	————	————	————	————	————●	○○○○○	○○○○○●		
	Demolition of Existing S-356 Pump Station				●●●●●	————	————	————	●●●●●	*****	*****	*****	●————	————●	
	Gated Spillway S-355W		*****	●●●●●	●●●●●	————	————	————●○○	○○○○○	○○○○○●					
	Removal of L-67C, Construct L-67D Levee and Gap in L-67C Levee N		●●●●●	*****	*****	*****	*****	●————	————	————	————●	○○○○○●			
	Removal of L-29 Levee and L-67 Extension Levee, Backfill L-67 Ext Canal					●●●●●	*****	*****	*****	●————	————	————●○○	○○○○○●		
P14N	CEPP North: Inflow Facilities Needed to Restore Northern WCA-3A and Move Additional Water South to Everglades	QQ, II													
	Validation Report		*****	*****	*****●										
	L-4 Degrade, Pump Station S-630		*****	*****	*****	●————	————	————●	○○○○○●						
	S-8 Pump Station Modifications		*****	*****	*****	●————	————	————	————●	○○○○○	○○○○○●				
	L-6 Diversion		*****	●————	————	————	————●	○○○○○	○○○○○●						
	Miami Canal Backfill/Vegetated Hammocks		●●●●●	*****	*****	*****	●————	————	————	————	————●	○○○○○	○○○○○●		
	L-5 Canal Improvements		●●●●●	*****	*****	●————	————	————	————	————	————●	○○○○○	○○○○○●		
P14NW	CEPP New Water: Seepage Management Needed to Move More Water into the Everglades														
	Validation Report		●●●●●	*****	*****●										
	Seepage Barrier Wall	V	●●●●●	●————	——●										
P15	CEPP EAA: Moves New Water South, Stores it, and Treats it Before Going to the Everglades ⁴	G, C, E													
	EAA Reservoir - A-2 STA		————	————●	○○○○○	○○○○○●									
	EAA Reservoir - Canal Conveyance Improvements to North New River and Miami River Canals		*****	*****	●————	————	————	————●	○○○○○●						
	EAA Reservoir - Seepage Canal (7.2 miles) and Inflow/Outflow Canal		————	————	————●	○○○○○	○○○○○●								
	EAA Reservoir - Foundation and Cutoff Wall		*****	●————	————	————	————	————	————●						
	EAA Reservoir - Embankment, Outlet Works and Inline Spillway		*****	*****	●●●●●	————	————	————	————	————	————●	○○○○○	○○○○○●		
	EAA Reservoir - S-636 Seepage Pump Station		●●●●●	*****	●●●●●	————	————	————	————●	○○○○○	○○○○○●				
	EAA Reservoir - Inflow Pump Station		*****	*****	●●●●●	————	————	————	————	————●	○○○○○	○○○○○●			



IDS 2023: CERP GENERATION 4, WRDA 2020



PROJECT LOCATOR	PROJECT	YELLOW BOOK COMPONENT	FISCAL YEAR (dollars in millions) ¹												
			2022 W	2023	2024 W	2025	2026 W	2027	2028 W	2029	2030 W	2031	2032 W	2033	2034 W
CERP GENERATION 4 (AUTHORIZED IN WRDA 2020)															
P16	Loxahatchee River Watershed Restoration Project	K, OPE	●-----	-----●	-----●										
	Flow-way 1 (M-1 Canal, G160/161 and Grassy Water Preserve)				●-----	-----	●-----	-----	-----●	◇◇◇◇●					
	Flow-way 2 (C-18 Impoundment)			●-----	-----	-----	---●-----	-----	-----	-----	-----	-----●	◇◇◇◇◇	◇◇◇◇●	
	Flow-way 2 (ASR Wells)							●-----	-----	-----	-----●	-----	-----●	◇◇◇◇●	
	Flow-way 3 Kitching Creek, Moonshine Creek, Gulfstream East, Cypress Creek Canal, Gulfstream West, and Palmar East)		●-----	-----	-----	-----	●-----	-----	-----	-----	-----	-----	-----●	◇◇◇◇◇	◇◇◇◇●





TOP 10 NAICS CODE CONTRACTS AWARDED FY2023



Rank	NAICS	NAICS Description	Actions	Dollars	% Dollars
1	237990	OTHER HEAVY AND CIVIL ENGINEERING CONSTRUCTION	327	\$608,236,835	78.69%
2	238160	ROOFING CONTRACTORS	35	\$72,769,906	9.41%
3	562910	REMEDIATION SERVICES	24	\$29,128,458	3.77%
4	541330	ENGINEERING SERVICES	133	\$13,112,565	1.70%
5	561210	FACILITIES SUPPORT SERVICES	30	\$8,605,928	1.11%
6	236220	COMMERCIAL AND INSTITUTIONAL BUILDING CONSTRUCTION	43	\$7,865,218	1.02%
7	541370	SURVEYING AND MAPPING (EXCEPT GEOPHYSICAL) SERVICES	176	\$7,151,512	0.93%
8	541620	ENVIRONMENTAL CONSULTING SERVICES	50	\$7,014,897	0.91%
9	237310	HIGHWAY, STREET, AND BRIDGE CONSTRUCTION	7	\$5,268,574	0.68%
10	541990	ALL OTHER PROFESSIONAL, SCIENTIFIC, AND TECHNICAL SERVICES	11	\$4,844,114	0.63%



U.S. ARMY

SMALL BUSINESS CONFERENCE (SBC) 2023



- The Jacksonville District was awarded HUBZone of the Year with an increase of over \$40M with total dollar value of \$78,515,989 in HUBZone awards and an overall goal achievement increase from 4.6% to 10.43%.
- The Jacksonville District was also recognized for executing awards for District or Center executing **50% or more of the contract awards to Small Business** in the amount of \$752,626,837 at 65.22%





U.S. ARMY



WE ARE HIRING!

Join the Jacksonville District Team



Seeking to fill multiple positions:

Biologist, Physical Scientist, Program Analyst, Engineers, Geologist, Chemist, Landscape Architect and many more.

Scan the QR Code




Or visit

www.saj.usace.army.mil/NowHiring



U.S. ARMY

JACKSONVILLE DISTRICT OFFICE OF SMALL BUSINESS PROGRAMS (OSBP)

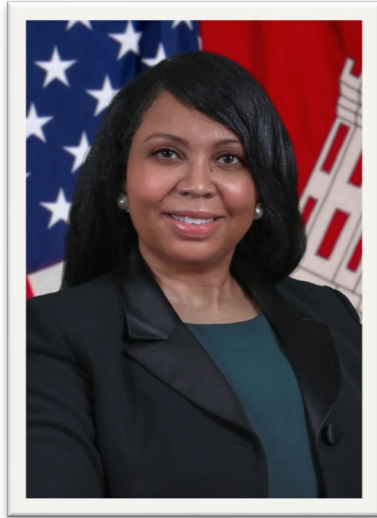

Kimberly S. Daniel-Ray

Chief, Office of Small Business Programs
USACE, Jacksonville District
Office: 904-232-1150 / Mobile: 904-577-3079

Nicole Batista-Cruz

Small Business Assistant
USACE, Jacksonville District
Office: 904-232-3275

Small Business Email:

SAJ-SB@usace.army.mil



U.S. ARMY

JACKSONVILLE DISTRICT SMALL BUSINESS WEBSITE





Jacksonville District Small Business Office



The Jacksonville Small Business Office develops small businesses and maximizes their opportunities to participate in Corps procurements, ensuring a broad base of capable suppliers to support the Corps' mission and strengthen the nation's economic development. The Small Business Program seeks Women Owned, B(a), Historically Underutilized Business Zone Empowerment (HubZone) and Service-Disabled Veteran-Owned businesses, as well as Historical Black Colleges and Universities, and Minority Institutions that are interested in doing business with the federal government.

Contact Us

Deputy, Small Business Programs
Kimberly S. Daniel-Ray

Small Business Office Phone:
904-577-3079

Small Business Email Address
SAJ-SB@usace.army.mil

Business With Us Links


- [SAD Small Business Website](#)
- [USACE Small Business Website](#)
- [Doing Business with USACE Districts](#)
- [Contracting in Puerto Rico](#)
- [What Small Businesses Need to Know](#)
- [Contract Security Requirements](#)
- [Small Business Basics](#)
- [Subcontracting Resources](#)
- [USACE Customer Outreach/Events](#)
- [Federal Business Opportunities](#)
- [Other Service Contracts](#)
- [Small Business Office](#)

Hurricane Response Opportunities

[Hurricane Relief contractors contact information](#)

Contractors Seeking Work

- The U.S. Army Corps of Engineers, Jacksonville District, is working with the full range of federal, state and local partners in response to Hurricane Fiona and the restoration work that will be required in its aftermath.
- Businesses and individual contractors interested in doing business with the U.S. Army Corps of Engineers should take the first step of registering with the System for Award Management (SAM)

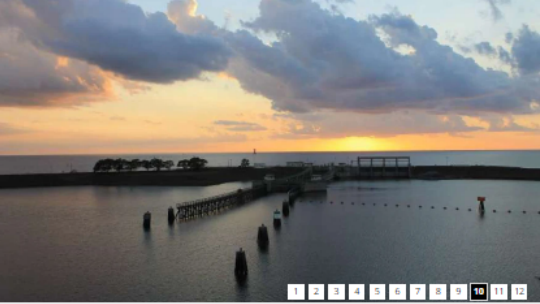

Top 10 NAICS Codes Contracts Awarded Fiscal Year 2023

Rank	NAICS	NAICS Description	Actions	Dollars	% Dollars
1	237990	OTHER HEAVY AND CIVIL ENGINEERING CONSTRUCTION	327	\$608,236,835	78.69%
2	238160	ROOFING CONTRACTORS	35	\$72,769,906	9.41%
3	562910	REMEDIAL SERVICES	24	\$29,128,458	3.77%
4	541330	ENGINEERING SERVICES	133	\$13,112,565	1.70%
5	561210	FACILITIES SUPPORT SERVICES	30	\$8,605,928	1.11%
6	236220	COMMERCIAL AND INSTITUTIONAL BUILDING CONSTRUCTION	43	\$7,865,218	1.02%
7	541370	SURVEYING AND MAPPING (EXCEPT GEOPHYSICAL) SERVICES	176	\$7,151,512	0.93%
8	541620	ENVIRONMENTAL CONSULTING SERVICES	50	\$7,014,897	0.91%
9	237310	HIGHWAY, STREET, AND BRIDGE CONSTRUCTION	7	\$5,268,574	0.68%
10	541990	ALL OTHER PROFESSIONAL, SCIENTIFIC, AND TECHNICAL SERVICES	11	\$4,844,114	0.63%

Forecast

JACKSONVILLE DISTRICT
FORECAST
FISCAL YEAR 2024-2028
SUBAD Office Code: W9-DEP
As of November 2023
Working Copy to Build a Better Tomorrow



[Click photo or link to view upcoming Forecast.](#)

Program Overview

JACKSONVILLE DISTRICT
PROGRAM OVERVIEW
SUBAD Office Code: W9-DEP
As of November 2023
Working Copy to Build a Better Tomorrow




[Click to view Program Overview](#)

Upcoming Events

2024 SAME Jax Post Industry Day, Wed, Jan. 10, 2024.

For more information: <https://samejax.org/>

JACKSONVILLE DISTRICT
UPCOMING EVENTS
FISCAL YEAR 2024
SUBAD Office Code: W9-DEP
As of November 2023
Working Copy to Build a Better Tomorrow



Search our Website to see:

- ☐ Forecast
- ☐ Program Overview
- ☐ Upcoming Events
- ☐ Contracts Awards-Subcontracting Opportunities
- ☐ Additional Resources

SB Website Link and QR Code:

<https://www.saj.usace.army.mil/SmallBusiness/>





U.S. ARMY

DOING BUSINESS WITH THE CORPS OF ENGINEERS



1. Know the mission and area of responsibility of USACE District.
2. Websites/social media - get smart on: www.beta.SAM.Gov, FPDS-NG, District websites, USASpending.gov
3. Take advantage of industry days, site visits and pre-proposals (free marketing).
4. Relationships - focus on relationships with the right people.
5. Familiarize yourself with DoD contracting regulations and procedures.
6. Consider Subcontracting opportunities.
7. Follow the funding.
8. READ! READ! READ!



U.S. ARMY

JACKSONVILLE DISTRICT: FORECAST - FY 2024

SEARCH SAM.GOV: W912EP*



Opportunity	Location	District / Center	Release Date (Qtr)	NAICS	Est Value	SBSA / Unrestricted	Solicitation Type
Brevard County, FL Mid Reach SPP	Brevard County, FL	SAJ	1st Qtr	237990	\$35,800,000	Unrestricted	Regional Dredging MATOC
Brevard County, FL South Reach SPP	Brevard County, FL	SAJ	1st Qtr	237990	\$16,000,000	Unrestricted	Regional Dredging MATOC
CAP: Lake Worth Lagoon, FL	Palm Beach County, FL	SAJ	1st Qtr	237990	\$14,400,000	Unrestricted	IFB
Kissimmee River Restoration Project, Contract 12A S-69 Weir Repair	Okeechobee, FL	SAJ	1st Qtr	237990	\$2,000,000	SBSA	IFB
Duval County, FL Shore Protection Project FY24 FCCE Emergency Renourishment	Duval County, FL	SAJ	1st Qtr	237990	\$24,000,000	Unrestricted	IFB
CEPP-South, CNT 3B, S-355W Gated Spillway Central Everglades Planning Project	Miami-Dade County, FL	SAJ	1st Qtr	237990	\$31,500,000	Unrestricted	RFP-BVTO
Jacksonville Harbor, FL (O&M) Combined w/Mayport NAS O&M	Jacksonville, FL	SAJ	1st Qtr	237990	\$33,640,000	Unrestricted	Regional Dredging MATOC
CEPP - CNT 2A S-356E	Miami-Dade County, FL	SAJ	3rd Qtr	237990	\$225,512,000	Unrestricted	RFP-BVTO
SAD 2024 Regional Dredging MATOC	Multiple locations within SAD	SAJ	3rd Qtr	237990	\$400,000,000	SBSA	RFP - All qualifying offerors, IAW FAR 15.304(c)(1)(ii)(A)
Palm Beach Hrb O&M FY 24 Maintenance Dredging	Palm Beach, FL	SAJ	1st Qtr	237990	\$5,000,000	Unrestricted	IFB
NSB Kings Bay Subase FY24 Maintenance Dredging	Camden County, GA	SAJ	3rd Qtr	237990	\$8,000,000	SBSA	IFB
Hurricane and Storm Damage Reduction Project, Flagler Beach Initial Nourishment	Flagler County, FL	SAJ	3rd Qtr	237990	\$25,000,000	Unrestricted	IFB
AIWW Norfolk to St Johns O&M Maintenance Dredging Sawpit Reach	St Johns County, FL	SAJ	3rd Qtr	237990	\$8,000,000	SBSA	IFB



U.S. ARMY

JACKSONVILLE DISTRICT: FORECAST - FY 2024

SEARCH SAM.GOV: W912EP*



Opportunity	Location	District / Center	Release Date (Qtr)	NAICS	Est Value	SBSA / Unrestricted	Solicitation Type
Port Everglades US Coast Guard Reconfiguration	Port Everglades, FL	SAJ	3rd Qtr	237990	TBD	Unrestricted	RFP-BVTO
St Lucie Inlet O&M Maintenance Dredging	St Lucie, FL	SAJ	3rd Qtr	237990	\$11,400,000	Unrestricted	IFB
O&M Ponce de Leon Inlet / O&M IWW near Ponce de Leon Inlet, Volusia County	Volusia County, FL	SAJ	4th Qtr	237990	\$8,000,000	SBSA	IFB
USMC O&M FY24 Dredging Event	Jacksonville, FL	SAJ	4th Qtr	237990	\$2,500,000	SBSA	IFB
IWW Crossroad and Jupiter	Jupiter Inlet, FL	SAJ	4th Qtr	237990	\$3,000,000	SBSA	IFB
Tampa Hrb DMMA 3D Maintenance	Tampa, FL	SAJ	4th Qtr	237990	\$10,000,000	SBSA	IFB
Brevard North Reach/Canaveral Sand Bypass	Brevard County, FL	SAJ	4th Qtr	237990	\$27,000,000	Unrestricted	IFB
BCWPA C-11 Impoundment, CNT 2	Broward County, FL	SAJ	4th Qtr	237990	\$350,000,000	Unrestricted	RFP-BVTO
IRL-S C23/C-24 North Reservoir - CNT 1	St Lucie County, FL	SAJ	4th Qtr	237990	\$100,000,000	Unrestricted	RFP-BVTO
HHD Pump Station S-4 and S-131 Stilling Well Replacements	Glades County, FL	SAJ	2nd Qtr	237990	\$3,000,000	SBSA	IFB
EAA Reservoir, Embankment and Outlet Structures CNT 11B	Palm Beach County, FL	SAJ	4th Qtr	237990	\$2,000,000,000	Unrestricted	RFP-BVTO
IRL-S C-44 Seepage Management Feature	Martin County, FL	SAJ	4th Qtr	237990	\$10,000,000	Unrestricted	RFP-BVTO
New QA Services for the Rest of Florida	All of Florida	SAJ	3rd	541990	\$40,000,000	SBSA	RFP
New QA Services for EAA	Port Everglades	SAJ	3rd	541990	\$45,000,000	SBSA	RFP
New EN Support Services	All of Florida	SAJ	2nd	541330	\$4,500,000	SBSA	RFP
Environmental Remediation Services	All of Florida	SAJ	1st	562910	\$24,000,000	SBSA	RFP



U.S. ARMY

JACKSONVILLE DISTRICT: FORECAST - FY 2024

SEARCH SAM.GOV: W912EP*

Opportunity	Location	District / Center	Release Date (Qtr)	NAICS	Est Value	SBSA / Unrestricted	Solicitation Type
Survey & Mapping (MATOC) "Topo/Hydrographic, Boundary, and SUE" IDIQ	FL	SAJ	2nd Qtr	5413700	\$30,000,000	SBSA	RFP / Brooks Act
Cost Engineering Support Florida	FL	SAJ	2nd Qtr	541330	\$250,000	Unrestricted	RFP / Brooks Act
St Johns County Vibracore Investigation	St. Johns County	SAJ	2nd Qtr	541330	\$420,000	SBSA	RFP / Brooks Act
FT. Buchanan Mogote Stabilization	Pueblo Viejo, Guaynabo, Puerto Rico	SAJ	3rd Qtr	541330	\$1,200,000	Unrestricted	RFP / Brooks Act
EDC Services for S-355W	Miami-Dade County	SAJ	2nd Qtr	541330	\$3,000,000	SBSA	RFP / Brooks Act
Flamingo Marina Bulkhead Rehabilitation	Miami, Florida	SAJ	3rd Qtr	237990	\$15,000,000	SBSA	RFP
Army Aviation Support Facility (AASF)	Fredericksburg, Virgin Island	SAJ	4th Qtr	237990	\$11,000,000	SBSA	RFP
Civil Support Team (CST) Ready Building	Fredericksburg, Virgin Island	SAJ	4th Qtr	237990	\$28,000,000	SBSA	RFP
Fort Allen Reception Station Renovation	San Juan, Puerto Rico	SAJ	4th Qtr	237990	\$13,000,000	SBSA	RFP
National Park Service Embankment Repairs	San Juan, Puerto Rico	SAJ	4th Qtr	237990	\$16,000,000	SBSA	RFP
Operation Division Multiple Award Task Order	All of Florida	SAJ	2nd Qtr	237990	\$49,000,000	SBSA	RFP



U.S. ARMY

JACKSONVILLE DISTRICT: AE BUSINESS OPPORTUNITIES

FY 2024-2025



SEARCH SAM.GOV: W912EP*

Opportunity	Location	Projected Advertise Date	Projected Award Date	NAICS Code	Est Value	SBSA / Unrestricted	Solicitation Type
Design IDIQ	Military	3rd Qtr. FY24	3rd Qtr. FY22	541330	\$20M	SB/Unrestricted	MATOC
Survey & Mapping "Topo/Hydrographic, Boundary, and SUE"	Primarily Florida	3rd Qtr. FY24	3rd Qtr. FY22	541370	\$30M	SB/Unrestricted	MATOC
Services Contract EN Div.	Primarily Florida	3rd Qtr. FY24	4th Qtr. FY23	541330	\$4.5M	SB	SAT
Geotech Drilling & Testing	Antilles	4th Qtr. FY24	4th Qtr. FY23	541330	\$15M	SB/Unrestricted	SATOC
Geotech Design	Florida Antilles	4th Qtr. FY24	2nd Qtr. FY25	541330	\$30M	TBD	SATOC
Geotech Drilling & Testing	Primarily Florida	2nd Qtr. FY25	2nd Qtr. FY25	541330	\$10M	TBD	SATOC

"These projections are based on the best information available. They are subject to modification and are in no way binding on the Government. More specific information relating to any individual item or class of items will not be furnished until the proposed acquisition is synopsized through SAM.gov or the solicitation is issued."



U.S. ARMY

JACKSONVILLE DISTRICT: AE TASK ORDERS FY 2024-2025

SEARCH SAM.GOV: W912EP*



Project Name	Anticipated Award Date
St Croix, USVI ARNG Readiness Center & Army Aviation Support Facility - Geotechnical Investigation	Jan-24
Ft Buchanan Mogote Stabilization Design	Jan-24
Fort Allen Readiness Center - Military Geotechnical Investigation	Jan-24
New Pass O&M Geotechnical Investigation	Jan-24
CEPP Adaptive Management Estimate & CEPP CSRA Update	Jan-24
C-44 Groundwater Qual Sampling - Phases 1 and 2	Feb-24
CEPP CNT 5 Levee	Mar-24
EDC Support Services for CERP S-355 Spillway	May-24
EDC Support Services for C-11 BCWPA, Florida	Jun-24

"These projections are based on the best information available. They are subject to modification and are in no way binding on the Government."



U.S. ARMY

UPCOMING EVENTS FY 2024



Date	Event	Location
January 10, 2024	SAME Jacksonville Post, Industry Day	Jacksonville, FL Link: https://samejax.org/index.php
February 5-7, 2024	National Small Business Conference The National 8(a) Association National Small Business Conference is the premier supplier diversity event for small businesses.	Atlanta, GA Link: https://www.national8aassociation.org/upcoming-events
February 15, 2024	SAME Space Coast Post Small Business Industry Day & Federal Contracting Workshop.	Cocoa Beach, FL Link: https://samespacecoast.org/
April 2024 TBD	USACE Charleston District - Industry Day	Charleston, SC Link: https://www.sac.usace.army.mil/business/
April 16-18, 2024	Southeast Regional Federal Construction Infrastructure & Environment Summit The Conference offers educational sessions, matchmaking, networking and resources for all small businesses.	Wilmington, NC Link: https://summit.ncmbc.us/



U.S. ARMY



FOR MORE INFORMATION

U.S. Army Corps of Engineers | Jacksonville District

<http://www.saj.usace.army.mil/>

Deputy, Office of Small Business Programs

(904) 232-1150

On Facebook www.facebook.com/JacksonvilleDistrict

On YouTube! www.youtube.com/JaxStrong


On Twitter www.twitter.com/JaxStrong

On Flickr www.flickr.com/photos/jaxstrong

Useful Restoration Sites:

www.evergladesrestoration.gov

www.sfwmd.gov

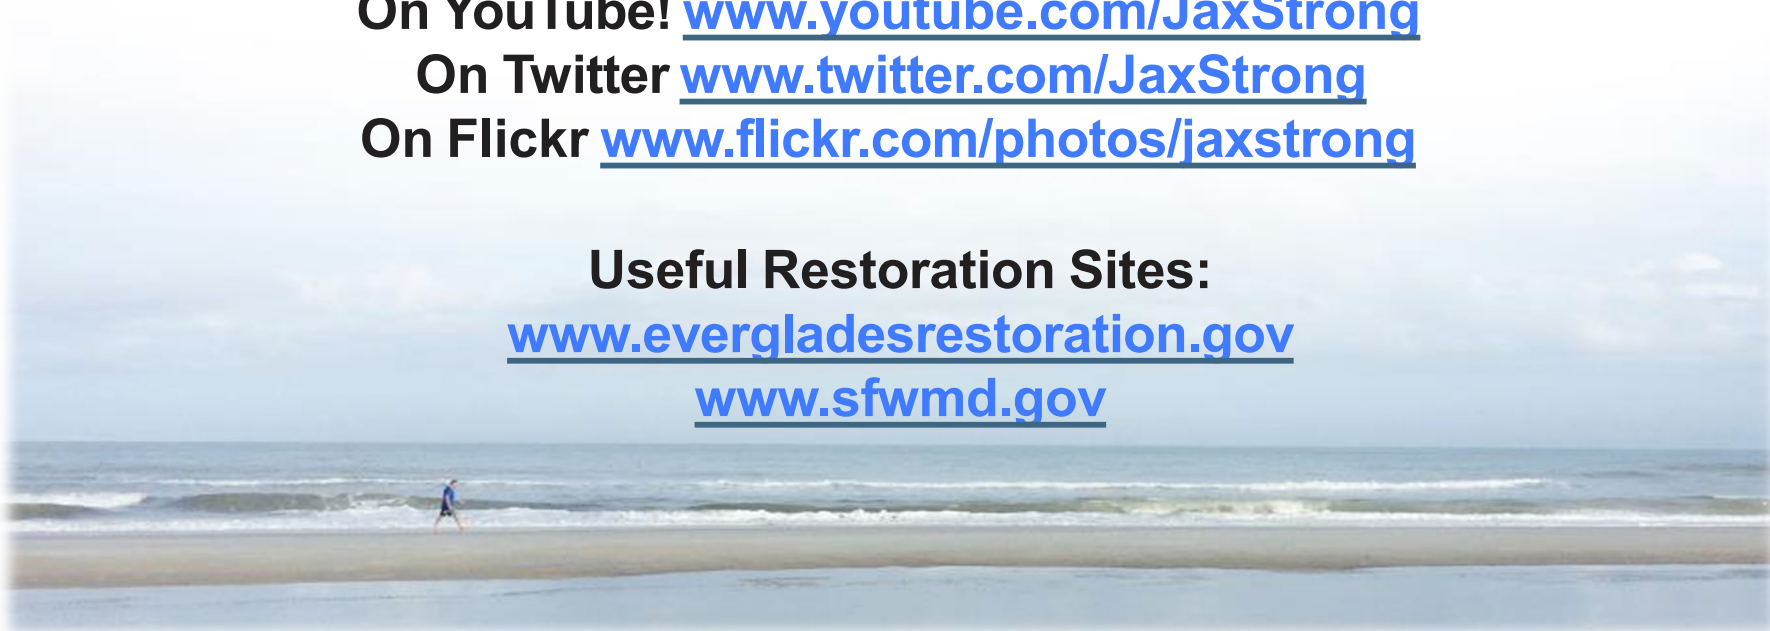



U.S. ARMY

PROCUREMENT ASSISTANCE



SB Resources

- Business Opportunity Specialist
- Procurement Center Representative
- Procurement Technical Assistant Center



Marketing Resources

- [Contract Opportunities on SAM.gov](#)
- [Contract Data on SAM.gov](#)
- [System for Award Management](#)
- [Dynamic Small Business Search System](#)
- [Subcontracting Networking System \(SubNet\)](#)



Other Resources

- [USASpending](#)
- [GSA Subcontracting Directory](#)
- [DoD Prime Contracting Directory](#)

